OWNER/DEVELOPER - THE HARBORVIEW COMPANY, LLC
CONSTRUCTION MANAGER - KSD GROUP, INC.
GENERAL CONTRACTOR - WEBCOR BUILDERS

THE HARBOR VIEW AT JACK LONDON SQUARE

121 - 129 SECOND STREET
OAKLAND, CA 94607

CONTRACT EXHIBIT "C"
STATUS DATE: April 15, 2005
Job No. 386

NO.	Name	DURATION	START	FINISH	%
1	**THE HARBOR VIEW - CONSTRUCTION**	**409 d**	**Wed 12/1/04**	**Mon 7/17/06**	**6%**
2	**Demolition & Earthwork**	**62 d**	**Wed 12/1/04**	**Fri 2/25/05**	**100%**
3	Hardscape Demo	3.2 wks	Wed 12/1/04	Wed 12/22/04	100%
4	***Inclement Weather Delay (12/27/04 thru 1/12/05)***	**13 d**	Mon 12/27/04	Wed 1/12/05	100%
5	Mass Excavation & Rough Grading	5 d	Mon 1/17/05	Fri 1/21/05	100%
6	***Unforeseen Soil Condition Delay (1/24/05)***	**1 d**	Mon 1/24/05	Mon 1/24/05	100%
7	Structural Excavation (Phase I)	7 d	Tue 1/25/05	Wed 2/2/05	100%
8	***Inclement Weather Delay (1/26/05)***	**1 d**	Wed 1/26/05	Wed 1/26/05	100%
9	Piles Installation (Phase I)	5 d	Thu 1/27/05	Wed 2/2/05	100%
10	***Soil Treatment Set Up Delay (2/03/05)***	**1 d**	Thu 2/3/05	Thu 2/3/05	100%
11	***Soil Treatment Delay (2/4/05 thru 2/10/05)***	**5 d**	Fri 2/4/05	Thu 2/10/05	100%
12	***Inclement Weather Delay (2/15/05 thru 2/22/05)***	**5 d**	Fri 2/11/05	Thu 2/17/05	100%
13	Structural Excavation (Phase II)	6 d	Fri 2/18/05	Fri 2/25/05	100%
14	**Piling**	**6 d**	**Tue 2/22/05**	**Tue 3/1/05**	**100%**
15	Piles Installation (Phase II)	6 d	Tue 2/22/05	Tue 3/1/05	100%
16	**Jobsite Equipment**	**234 d**	**Mon 3/28/05**	**Thu 3/2/06**	**12%**
17	**Tower Crane**	**156 d**	**Mon 3/28/05**	**Mon 11/7/05**	**60%**
18	Tower Crane Erection	3 d	Mon 3/28/05	Wed 3/30/05	100%
19	Dismantle Tower Crane	2 d	Fri 11/4/05	Mon 11/7/05	0%
20	**Man lift**	**164 d**	**Thu 7/7/05**	**Thu 3/2/06**	**0%**
21	Install Man lift	5 d	Thu 7/7/05	Wed 7/13/05	0%
22	Remove Man lift	5 d	Fri 2/24/06	Thu 3/2/06	0%
23	**Scaffolding**	**71 d**	**Fri 11/4/05**	**Fri 2/17/06**	**0%**
24	Install Scaffold	5 d	Fri 11/4/05	Thu 11/10/05	0%
25	Remove Scaffold	5 d	Mon 2/13/06	Fri 2/17/06	0%
26	**Structural Concrete**	**192 d**	**Wed 2/2/05**	**Thu 11/3/05**	**18%**
27	**First Floor**	**64 d**	**Wed 2/2/05**	**Mon 5/2/05**	**60%**
28	**South**	**54 d**	**Wed 2/2/05**	**Mon 4/18/05**	**95%**
29	**Foundations**	**38 d**	**Wed 2/2/05**	**Fri 3/25/05**	**100%**
30	Form Footings	3 d	Wed 2/2/05	Fri 2/4/05	100%
31	Rebar	18 d	Tue 2/8/05	Thu 3/3/05	100%
32	***Inclement Weather Delay (2/28, 3/02, 3/04/05)***	**3 d**	Fri 3/4/05	Tue 3/8/05	100%
33	Template & Dowels	3 d	Wed 3/9/05	Fri 3/11/05	100%
34	***Inclement Weather Delay (3/18/05)***	**1 d**	Mon 3/14/05	Mon 3/14/05	100%
35	***Inclement Weather Delay (3/22/05 thru 3/23/05)***	**2 d**	Tue 3/15/05	Wed 3/16/05	100%
36	***Inclement Weather Delay (3/29/05 thru 3/30/05)***	**2 d**	Thu 3/17/05	Fri 3/18/05	100%
37	Place Foundations	4 d	Mon 3/21/05	Thu 3/24/05	100%
38	Strip & Layout	4 d	Tue 3/22/05	Fri 3/25/05	100%
39	**Vertical**	**5 d**	**Fri 3/25/05**	**Thu 3/31/05**	**100%**
40	**Columns**	**5 d**	**Fri 3/25/05**	**Thu 3/31/05**	**100%**
41	Set Rebar Cages	4 d	Fri 3/25/05	Wed 3/30/05	100%
42	Form, Pour, & Strip Columns	4 d	Mon 3/28/05	Thu 3/31/05	100%
43	**Slab on Grade**	**18 d**	**Thu 3/24/05**	**Mon 4/18/05**	**83%**

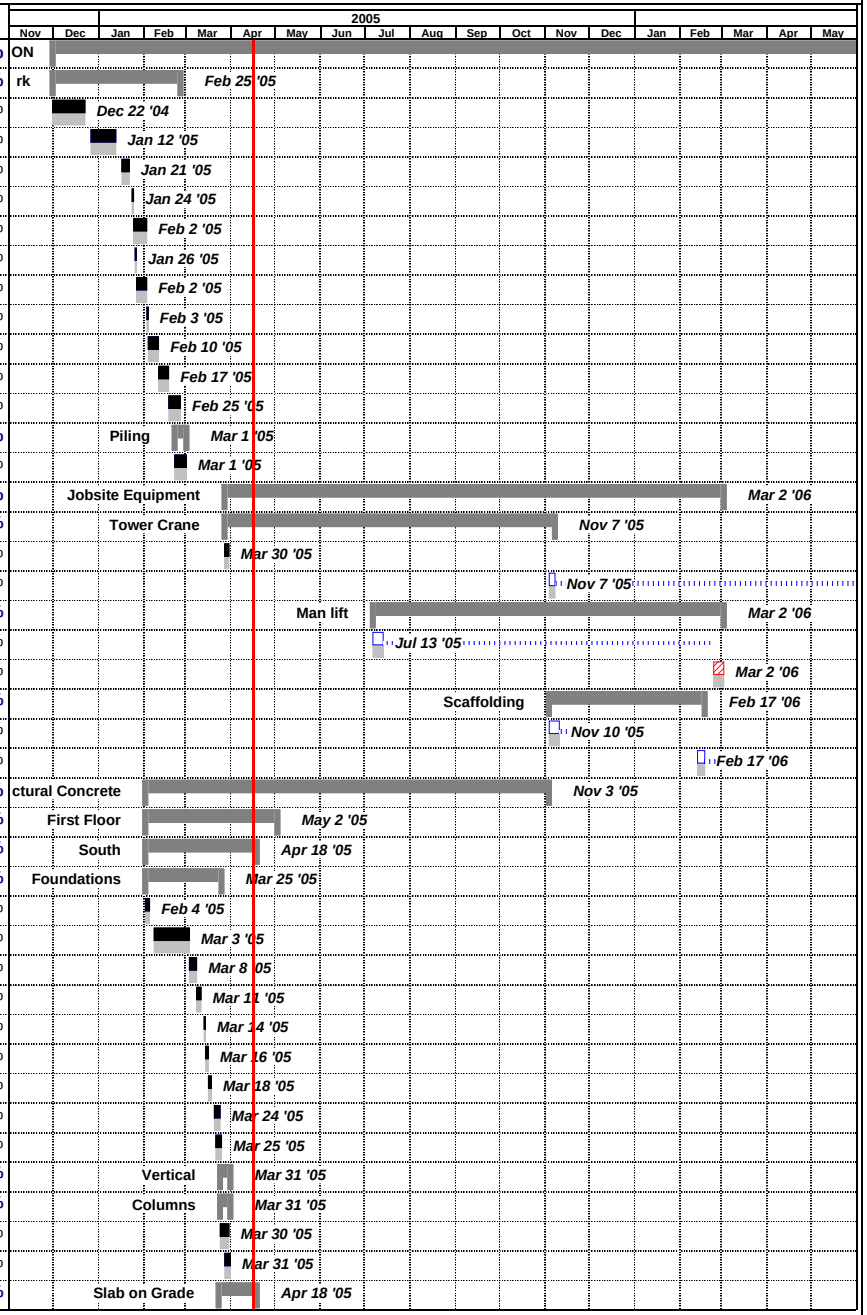

START DATE: DECEMBER 01, 2004
TCO DATE: JUNE 01, 2006
FINISH DATE: JULY 17, 2006

Actual Summary | Task | Task Progress | Actual Milestone | Deadline
Baseline | Critical Task | Baseline Milestone | Float

OWNER/DEVELOPER - THE HARBORVIEW COMPANY, LLC
CONSTRUCTION MANAGER - KSD GROUP, INC.
GENERAL CONTRACTOR - WEBCOR BUILDERS

THE HARBOR VIEW AT JACK LONDON SQUARE
121 - 129 SECOND STREET
OAKLAND, CA 94607

CONTRACT EXHIBIT "C"
STATUS DATE: April 15, 2005
Job No. 386

NO.	Name	DURATION	START	FINISH	%
44	Subslab MEP	8 d	Thu 3/24/05	Mon 4/4/05	100%
45	Visqueen (Weather Protection)	3 d	Tue 4/5/05	Thu 4/7/05	100%
46	***Inclement Weather Delay (4/04, 4/07, 4/08/05)***	**3 d**	Fri 4/8/05	Tue 4/12/05	100%
47	***Inclement Weather Delay (4/11/05)***	**1 d**	Wed 4/13/05	Wed 4/13/05	100%
48	Rebar & Place	3 d	Thu 4/14/05	Mon 4/18/05	0%
49	**North**	39 d	Wed 3/9/05	Mon 5/2/05	0%
50	**2nd Floor**	**25 d**	**Fri 4/29/05**	**Mon 6/6/05**	**0%**
51	**East**	**18 d**	**Fri 4/29/05**	**Tue 5/24/05**	**0%**
52	**Deck**	**13 d**	**Fri 4/29/05**	**Tue 5/17/05**	**0%**
53	Form Deck	4 d	Fri 4/29/05	Wed 5/4/05	0%
54	MEPs cans & inserts	3 d	Thu 5/5/05	Mon 5/9/05	0%
55	Rebar & Conduit	4 d	Tue 5/10/05	Fri 5/13/05	0%
56	Cast Ramp	1 d	Fri 5/13/05	Fri 5/13/05	0%
57	Cast East Deck	1 d	Tue 5/17/05	Tue 5/17/05	0%
58	**Vertical**	**5 d**	**Wed 5/18/05**	**Tue 5/24/05**	**0%**
59	Double Upturns w/Columns	3 d	Wed 5/18/05	Fri 5/20/05	0%
60	Cast & Strip Vertical	2 d	Mon 5/23/05	Tue 5/24/05	0%
61	**West**	**21 d**	**Thu 5/5/05**	**Mon 6/6/05**	**0%**
62	**Deck**	**15 d**	**Thu 5/5/05**	**Wed 5/25/05**	**0%**
63	Form Deck	6 d	Thu 5/5/05	Thu 5/12/05	0%
64	MEPs cans & inserts	3 d	Fri 5/13/05	Tue 5/17/05	0%
65	Rebar & Conduit	5 d	Wed 5/18/05	Tue 5/24/05	0%
66	Cast West Deck	1 d	Wed 5/25/05	Wed 5/25/05	0%
67	Vertical	6 d	Thu 5/26/05	Mon 6/6/05	0%
68	**Plaza Level**	**28 d**	**Wed 5/25/05**	**Wed 7/6/05**	**0%**
69	**East**	**19 d**	**Wed 5/25/05**	**Wed 6/22/05**	**0%**
70	**Deck**	**13 d**	**Wed 5/25/05**	**Tue 6/14/05**	**0%**
71	Form Deck	4 d	Wed 5/25/05	Wed 6/1/05	0%
72	Layout On Formwork	2 d	Thu 6/2/05	Fri 6/3/05	0%
73	MEPs cans & inserts	2 d	Mon 6/6/05	Tue 6/7/05	0%
74	Rebar & Conduit	4 d	Wed 6/8/05	Mon 6/13/05	0%
75	Cast	1 d	Tue 6/14/05	Tue 6/14/05	0%
76	Vertical	6 d	Wed 6/15/05	Wed 6/22/05	0%
77	**West**	**21 d**	**Tue 6/7/05**	**Wed 7/6/05**	**0%**
78	**Deck**	**16 d**	**Tue 6/7/05**	**Tue 6/28/05**	**0%**
79	Form Deck	6 d	Tue 6/7/05	Tue 6/14/05	0%
80	Layout On Formwork	2 d	Wed 6/15/05	Thu 6/16/05	0%
81	MEPs cans & inserts	2 d	Fri 6/17/05	Mon 6/20/05	0%
82	Rebar & Conduit	4 d	Tue 6/21/05	Fri 6/24/05	0%
83	Surface Depressions & Screeds	2 d	Fri 6/24/05	Mon 6/27/05	0%
84	Cast	1 d	Tue 6/28/05	Tue 6/28/05	0%
85	Vertical	5 d	Wed 6/29/05	Wed 7/6/05	0%
86	**4th Level**	**23 d**	**Thu 6/23/05**	**Tue 7/26/05**	**0%**

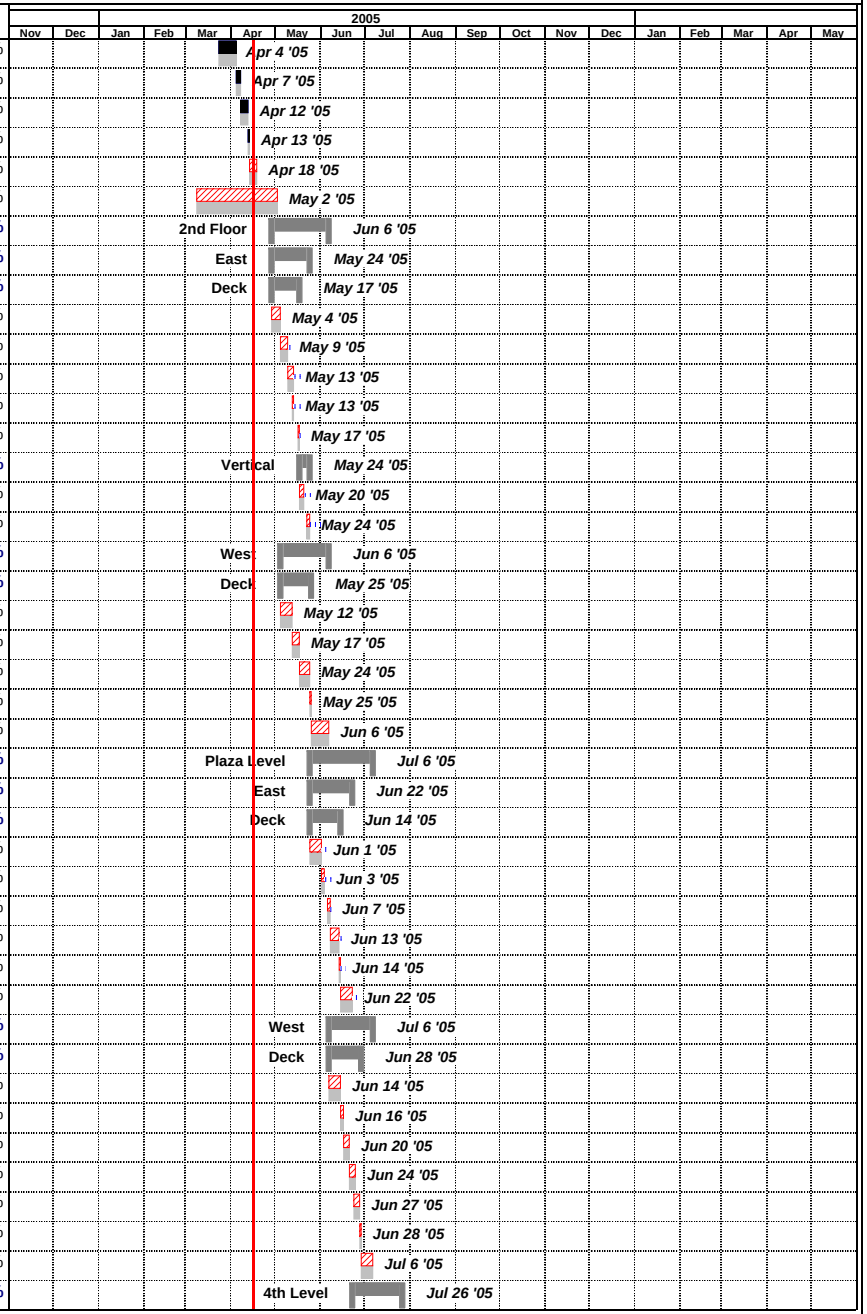

START DATE: DECEMBER 01, 2004
TCO DATE: JUNE 01, 2006
FINISH DATE: JULY 17, 2006

Actual Summary | Task | Task Progress | Actual Milestone | Deadline
Baseline | Critical Task | Baseline Milestone | Float

OWNER/DEVELOPER - THE HARBORVIEW COMPANY, LLC
CONSTRUCTION MANAGER - KSD GROUP, INC.
GENERAL CONTRACTOR - WEBCOR BUILDERS

THE HARBOR VIEW AT JACK LONDON SQUARE

121 - 129 SECOND STREET
OAKLAND, CA 94607

CONTRACT EXHIBIT "C"
STATUS DATE: April 15, 2005
Job No. 386

NO.	Name	DURATION	START	FINISH	%
87	**East**	**15 d**	**Thu 6/23/05**	**Thu 7/14/05**	**0%**
88	**Deck**	**10 d**	**Thu 6/23/05**	**Thu 7/7/05**	**0%**
89	Form Deck	4 d	Thu 6/23/05	Tue 6/28/05	0%
90	MEPs cans & inserts	2 d	Tue 6/28/05	Wed 6/29/05	0%
91	Rebar & Conduit	4 d	Thu 6/30/05	Wed 7/6/05	0%
92	Cast	1 d	Thu 7/7/05	Thu 7/7/05	0%
93	Vertical	5 d	Fri 7/8/05	Thu 7/14/05	0%
94	West	14 d	Thu 7/7/05	Tue 7/26/05	0%
95	**5th Level**	**22 d**	**Fri 7/15/05**	**Mon 8/15/05**	**0%**
96	East	14 d	Fri 7/15/05	Wed 8/3/05	0%
97	West	14 d	Wed 7/27/05	Mon 8/15/05	0%
98	**6th Level**	**22 d**	**Thu 8/4/05**	**Tue 9/6/05**	**0%**
99	East	14 d	Thu 8/4/05	Tue 8/23/05	0%
100	West	14 d	Tue 8/16/05	Tue 9/6/05	0%
101	**7th Level**	**22 d**	**Wed 8/24/05**	**Mon 9/26/05**	**0%**
102	East	14 d	Wed 8/24/05	Wed 9/14/05	0%
103	West	14 d	Wed 9/7/05	Mon 9/26/05	0%
104	**8th Level**	**22 d**	**Thu 9/15/05**	**Fri 10/14/05**	**0%**
105	East	14 d	Thu 9/15/05	Tue 10/4/05	0%
106	West	14 d	Tue 9/27/05	Fri 10/14/05	0%
107	**Roof Level**	**22 d**	**Wed 10/5/05**	**Thu 11/3/05**	**0%**
108	East	14 d	Wed 10/5/05	Mon 10/24/05	0%
109	West	14 d	Mon 10/17/05	Thu 11/3/05	0%
110	**Exterior**	**156 d**	**Tue 8/16/05**	**Thu 3/30/06**	**0%**
111	1st & 2nd Floor CMU Along Gridline 3	3 wks	Tue 8/16/05	Wed 9/7/05	0%
112	**Elevator Penthouse**	**15 d**	**Wed 11/9/05**	**Thu 12/1/05**	**0%**
113	Frame	5 d	Wed 11/9/05	Tue 11/15/05	0%
114	Plaster	10 d	Wed 11/16/05	Thu 12/1/05	0%
115	Roofing	4 wks	Fri 12/2/05	Fri 12/30/05	0%
116	**Windows & Storefronts**	**76 d**	**Tue 8/16/05**	**Mon 12/5/05**	**0%**
117	3rd Floor - Windows In Concrete	10 d	Tue 8/16/05	Mon 8/29/05	0%
118	4th Floor - Windows In Concrete	10 d	Tue 8/30/05	Wed 9/14/05	0%
119	5th Floor - Windows In Concrete	10 d	Thu 9/15/05	Wed 9/28/05	0%
120	6th Floor - Windows In Concrete	10 d	Thu 9/29/05	Wed 10/12/05	0%
121	7th Floor - Windows In Concrete	10 d	Thu 10/13/05	Wed 10/26/05	0%
122	8th Floor - Windows In Concrete	10 d	Thu 10/27/05	Wed 11/9/05	0%
123	Storefronts & Garage Screens	4 wks	Fri 11/4/05	Mon 12/5/05	0%
124	**Plaster**	**54 d**	**Fri 11/11/05**	**Wed 2/1/06**	**0%**
125	**East line 3**	**47 d**	**Fri 11/11/05**	**Fri 1/20/06**	**0%**
126	Sheetmetal At Windows & Plaster	8 d	Fri 11/11/05	Tue 11/22/05	0%
127	Framing & Densglass	10 d	Wed 11/23/05	Thu 12/8/05	0%
128	Lathe	5 d	Fri 12/9/05	Thu 12/15/05	0%
129	Trim	5 d	Fri 12/16/05	Thu 12/22/05	0%

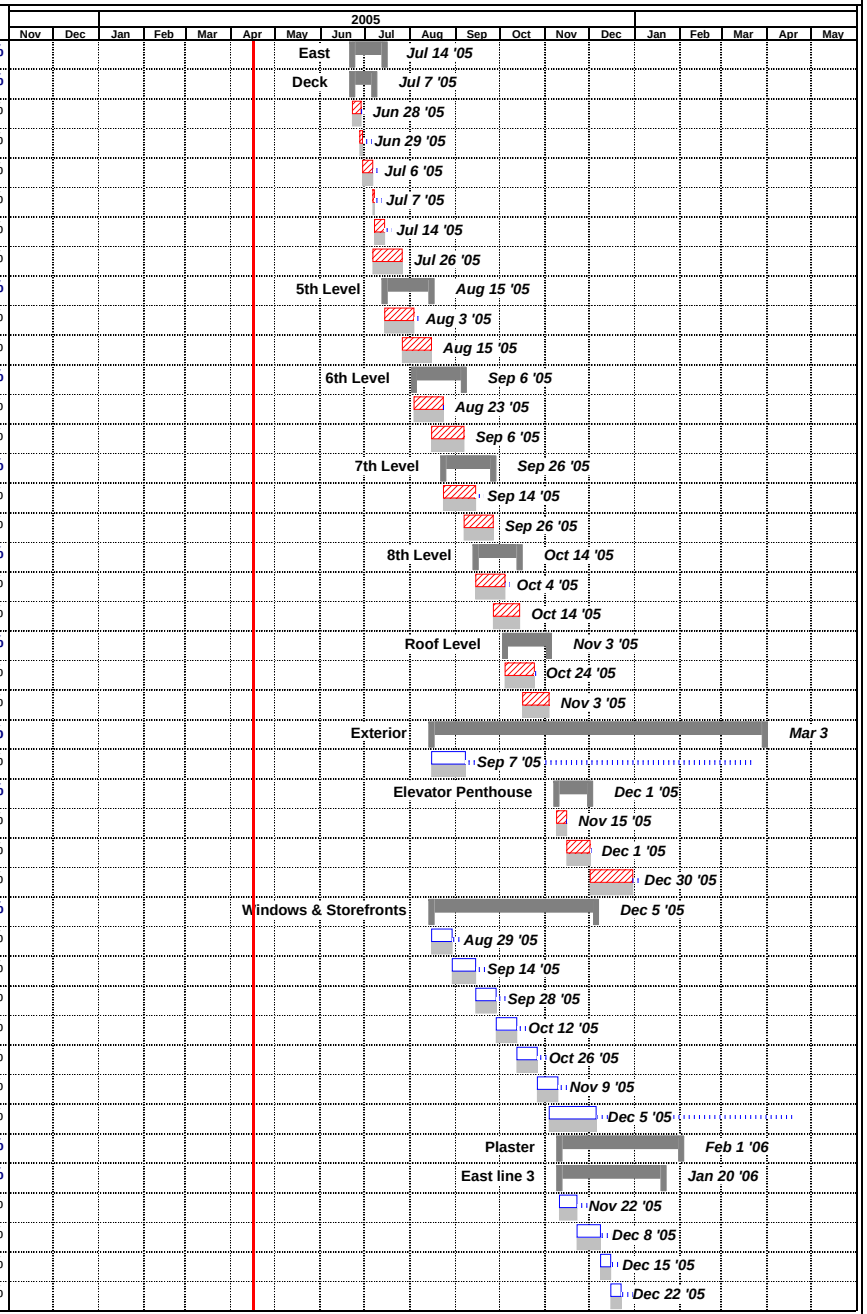

START DATE: DECEMBER 01, 2004
TCO DATE: JUNE 01, 2006
FINISH DATE: JULY 17, 2006

Actual Summary | Task | Task Progress | Actual Milestone | Deadline
Baseline | Critical Task | Baseline Milestone | Float

OWNER/DEVELOPER - THE HARBORVIEW COMPANY, LLC
CONSTRUCTION MANAGER - KSD GROUP, INC.
GENERAL CONTRACTOR - WEBCOR BUILDERS

THE HARBOR VIEW AT JACK LONDON SQUARE
121 - 129 SECOND STREET
OAKLAND, CA 94607

CONTRACT EXHIBIT "C"
STATUS DATE: April 15, 2005
Job No. 386

NO.	Name	DURATION	START	FINISH	%
130	Scratch Coat	3 d	Fri 12/23/05	Wed 12/28/05	0%
131	Brown Coat	3 d	Fri 1/6/06	Tue 1/10/06	0%
132	Finish Coat	3 d	Wed 1/18/06	Fri 1/20/06	0%
133	**Courtyard Elevation**	**48 d**	**Mon 11/21/05**	**Wed 2/1/06**	**0%**
134	Sheetmetal At Windows & Plaster	8 d	Mon 11/21/05	Fri 12/2/05	0%
135	Framing	10 d	Tue 12/6/05	Mon 12/19/05	0%
136	Lathe	5 d	Tue 12/20/05	Tue 12/27/05	0%
137	Trim	5 d	Wed 12/28/05	Wed 1/4/06	0%
138	Scratch Coat	3 d	Thu 1/5/06	Mon 1/9/06	0%
139	Brown Coat	3 d	Tue 1/17/06	Thu 1/19/06	0%
140	Finish Coat	3 d	Mon 1/30/06	Wed 2/1/06	0%
141	Exterior Infill at Man lift	4 wks	Fri 3/3/06	Thu 3/30/06	0%
142	Exterior Paint	8 wks	Wed 12/14/05	Fri 2/10/06	0%
143	**Landscape Work**	**59 d**	**Mon 2/20/06**	**Thu 5/11/06**	**0%**
144	Plaza Deck	10 wks	Mon 2/20/06	Fri 4/28/06	0%
145	Ground Level Site Work	6 wks	Fri 3/31/06	Thu 5/11/06	0%
146	**Interior Rough Out**	**121 d**	**Thu 7/7/05**	**Thu 12/29/05**	**0%**
147	**Vertical Risers MEPS**	**65 d**	**Thu 7/7/05**	**Fri 10/7/05**	**0%**
148	Fire Sprinkler	13 wks	Thu 7/7/05	Fri 10/7/05	0%
149	Electrical	13 wks	Thu 7/7/05	Fri 10/7/05	0%
150	Plumbing	13 wks	Thu 7/7/05	Fri 10/7/05	0%
151	Mechanical	13 wks	Thu 7/7/05	Fri 10/7/05	0%
152	**1st Floor Rough**	**29 d**	**Wed 7/27/05**	**Wed 9/7/05**	**0%**
153	Sprinkler	3 wks	Wed 7/27/05	Tue 8/16/05	0%
154	Framing	2 wks	Fri 8/12/05	Thu 8/25/05	0%
155	Rough Plumbing	2 wks	Fri 8/19/05	Thu 9/1/05	0%
156	Rough elec.	2 wks	Fri 8/19/05	Thu 9/1/05	0%
157	Rough HVAC	2 wks	Fri 8/19/05	Thu 9/1/05	0%
158	Electrical Inspection	1 d	Tue 9/6/05	Tue 9/6/05	0%
159	Plumbing inspection	1 d	Tue 9/6/05	Tue 9/6/05	0%
160	Close-up inspection	1 d	Wed 9/7/05	Wed 9/7/05	0%
161	**2nd Floor Rough**	**29 d**	**Wed 8/17/05**	**Wed 9/28/05**	**0%**
162	Sprinkler	3 wks	Wed 8/17/05	Thu 9/8/05	0%
163	Framing	2 wks	Tue 9/6/05	Mon 9/19/05	0%
164	Rough Plumbing	2 wks	Tue 9/13/05	Mon 9/26/05	0%
165	Rough elec.	2 wks	Tue 9/13/05	Mon 9/26/05	0%
166	Rough HVAC	2 wks	Tue 9/13/05	Mon 9/26/05	0%
167	Electrical Inspection	1 d	Tue 9/27/05	Tue 9/27/05	0%
168	Plumbing inspection	1 d	Tue 9/27/05	Tue 9/27/05	0%
169	Close-up inspection	1 d	Wed 9/28/05	Wed 9/28/05	0%
170	**3rd Floor Rough**	**29 d**	**Mon 8/29/05**	**Mon 10/10/05**	**0%**
171	Sprinkler	2 wks	Mon 8/29/05	Tue 9/13/05	0%
172	Framing	2 wks	Fri 9/9/05	Thu 9/22/05	0%

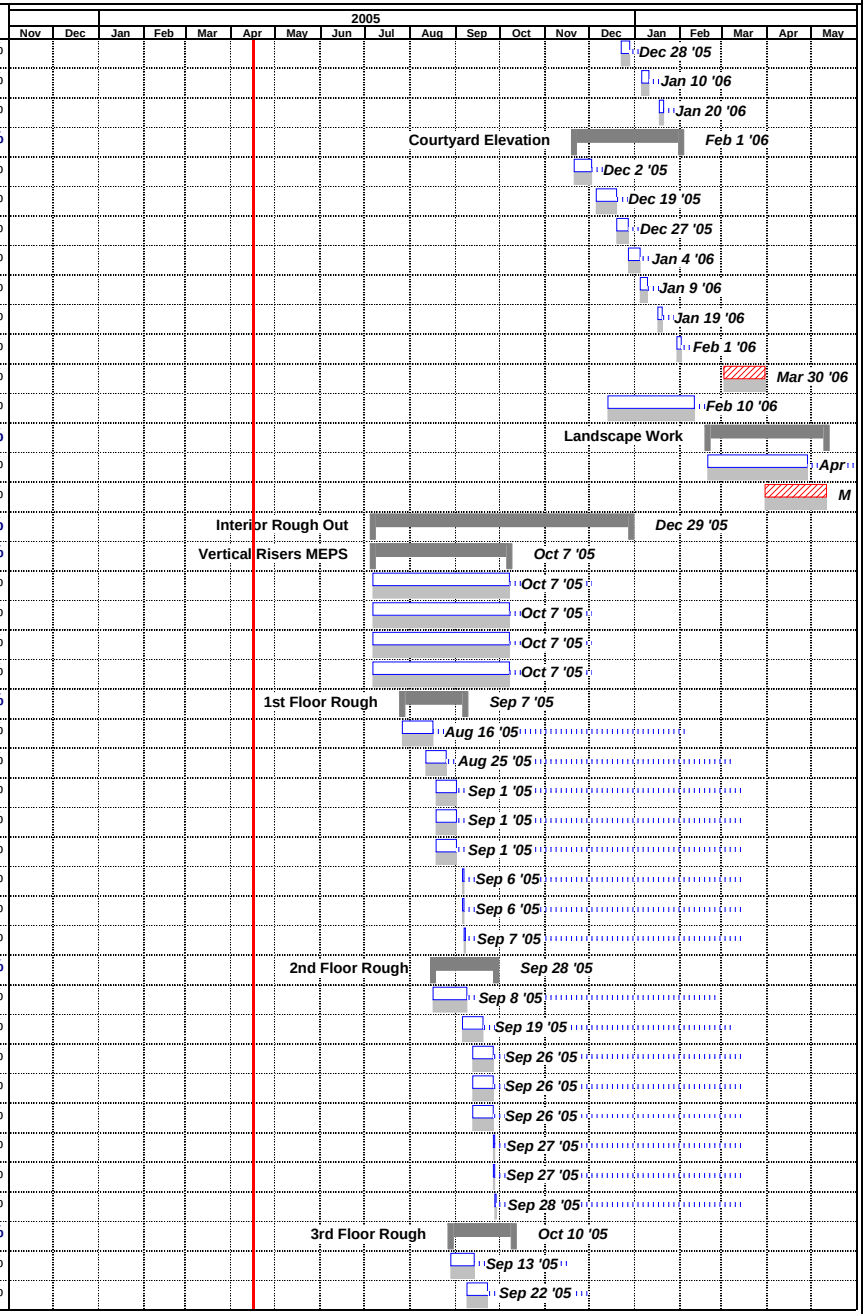

START DATE: DECEMBER 01, 2004
TCO DATE: JUNE 01, 2006
FINISH DATE: JULY 17, 2006

Actual Summary | Task | Task Progress | Actual Milestone | Deadline
Baseline | Critical Task | Baseline Milestone | Float

OWNER/DEVELOPER - THE HARBORVIEW COMPANY, LLC
CONSTRUCTION MANAGER - KSD GROUP, INC.
GENERAL CONTRACTOR - WEBCOR BUILDERS

THE HARBOR VIEW AT JACK LONDON SQUARE

121 - 129 SECOND STREET
OAKLAND, CA 94607

CONTRACT EXHIBIT "C"
STATUS DATE: April 15, 2005
Job No. 386

NO.	Name	DURATION	START	FINISH	%
173	Rough Plumbing	3 wks	Fri 9/16/05	Thu 10/6/05	0%
174	Rough Electrical	3 wks	Fri 9/16/05	Thu 10/6/05	0%
175	Rough HVAC	3 wks	Fri 9/16/05	Thu 10/6/05	0%
176	Electrical Inspection	1 d	Fri 10/7/05	Fri 10/7/05	0%
177	Plumbing inspection	1 d	Fri 10/7/05	Fri 10/7/05	0%
178	Close-up inspection	1 d	Mon 10/10/05	Mon 10/10/05	0%
179	**4th Floor Rough**	**29 d**	**Wed 9/14/05**	**Mon 10/24/05**	**0%**
180	Sprinkler	2 wks	Wed 9/14/05	Tue 9/27/05	0%
181	Framing	2 wks	Fri 9/23/05	Thu 10/6/05	0%
182	Rough Plumbing	3 wks	Fri 9/30/05	Thu 10/20/05	0%
183	Rough Electrical	3 wks	Fri 9/30/05	Thu 10/20/05	0%
184	Rough HVAC	3 wks	Fri 9/30/05	Thu 10/20/05	0%
185	Electrical Inspection	1 d	Fri 10/21/05	Fri 10/21/05	0%
186	Plumbing inspection	1 d	Fri 10/21/05	Fri 10/21/05	0%
187	Close-up inspection	1 d	Mon 10/24/05	Mon 10/24/05	0%
188	**5th Floor Rough**	**29 d**	**Wed 9/28/05**	**Mon 11/7/05**	**0%**
189	Sprinkler	2 wks	Wed 9/28/05	Tue 10/11/05	0%
190	Framing	2 wks	Fri 10/7/05	Thu 10/20/05	0%
191	Rough Plumbing	3 wks	Fri 10/14/05	Thu 11/3/05	0%
192	Rough Electrical	3 wks	Fri 10/14/05	Thu 11/3/05	0%
193	Rough HVAC	3 wks	Fri 10/14/05	Thu 11/3/05	0%
194	Electrical Inspection	1 d	Fri 11/4/05	Fri 11/4/05	0%
195	Plumbing inspection	1 d	Fri 11/4/05	Fri 11/4/05	0%
196	Close-up inspection	1 d	Mon 11/7/05	Mon 11/7/05	0%
197	**6th Floor Rough**	**29 d**	**Wed 10/12/05**	**Mon 11/21/05**	**0%**
198	Sprinkler	2 wks	Wed 10/12/05	Tue 10/25/05	0%
199	Framing	2 wks	Fri 10/21/05	Thu 11/3/05	0%
200	Rough Plumbing	3 wks	Fri 10/28/05	Thu 11/17/05	0%
201	Rough Electrical	3 wks	Fri 10/28/05	Thu 11/17/05	0%
202	Rough HVAC	3 wks	Fri 10/28/05	Thu 11/17/05	0%
203	Electrical Inspection	1 d	Fri 11/18/05	Fri 11/18/05	0%
204	Plumbing inspection	1 d	Fri 11/18/05	Fri 11/18/05	0%
205	Close-up inspection	1 d	Mon 11/21/05	Mon 11/21/05	0%
206	**7th Floor Rough**	**29 d**	**Wed 10/26/05**	**Wed 12/7/05**	**0%**
207	Sprinkler	2 wks	Wed 10/26/05	Tue 11/8/05	0%
208	Framing	2 wks	Fri 11/4/05	Thu 11/17/05	0%
209	Rough Plumbing	3 wks	Fri 11/11/05	Mon 12/5/05	0%
210	Rough Electrical	3 wks	Fri 11/11/05	Mon 12/5/05	0%
211	Rough HVAC	3 wks	Fri 11/11/05	Mon 12/5/05	0%
212	Electrical Inspection	1 d	Tue 12/6/05	Tue 12/6/05	0%
213	Plumbing inspection	1 d	Tue 12/6/05	Tue 12/6/05	0%
214	Close-up inspection	1 d	Wed 12/7/05	Wed 12/7/05	0%
215	**8th Floor Rough**	**27 d**	**Fri 11/18/05**	**Thu 12/29/05**	**0%**

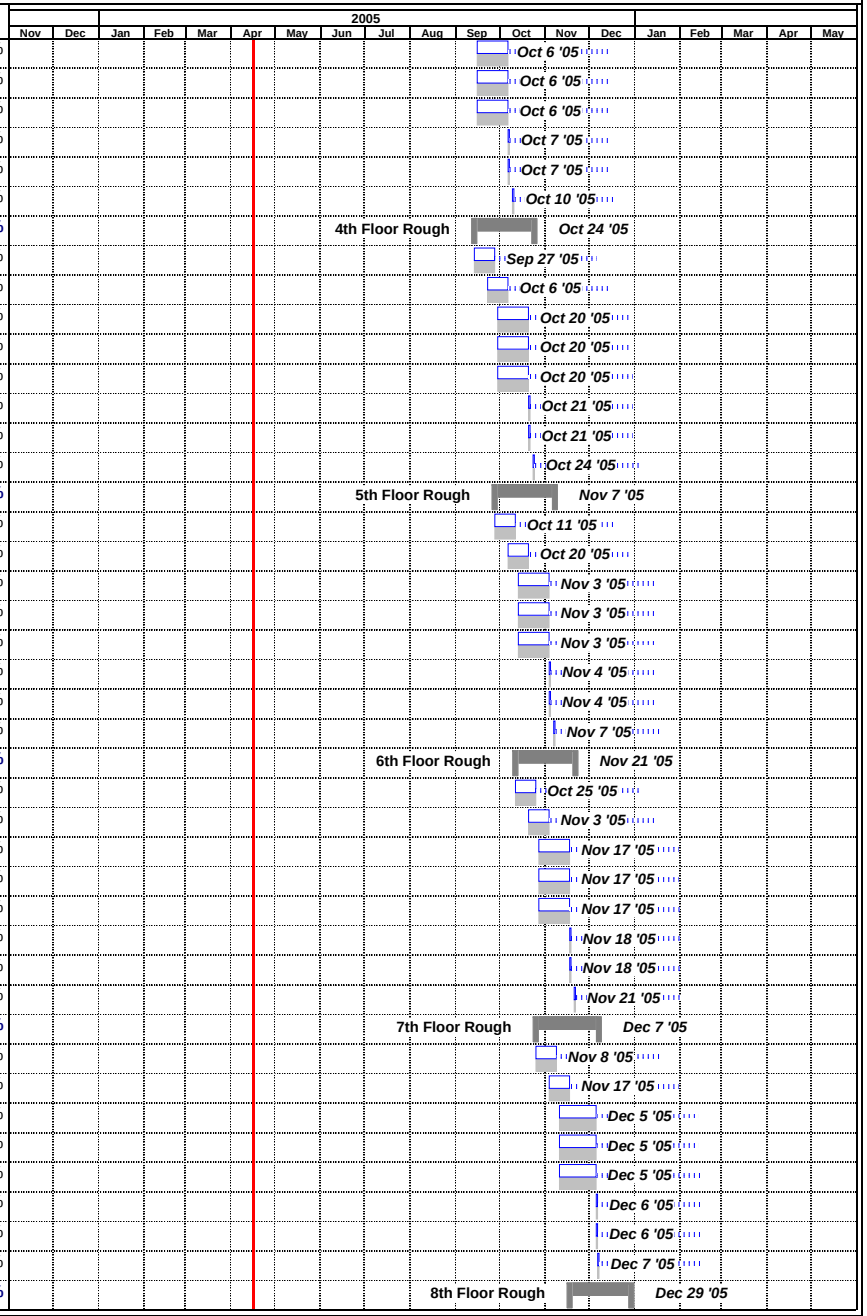

START DATE: DECEMBER 01, 2004
TCO DATE: JUNE 01, 2006
FINISH DATE: JULY 17, 2006

Actual Summary | Task | Task Progress | Actual Milestone | Deadline
Baseline | Critical Task | Baseline Milestone | Float

OWNER/DEVELOPER - THE HARBORVIEW COMPANY, LLC
CONSTRUCTION MANAGER - KSD GROUP, INC.
GENERAL CONTRACTOR - WEBCOR BUILDERS

THE HARBOR VIEW AT JACK LONDON SQUARE
121 - 129 SECOND STREET
OAKLAND, CA 94607

CONTRACT EXHIBIT "C"
STATUS DATE: April 15, 2005
Job No. 386

NO.	Name	DURATION	START	FINISH	%
216	Sprinkler	2 wks	Fri 11/18/05	Mon 12/5/05	0%
217	Framing	2 wks	Tue 11/29/05	Mon 12/12/05	0%
218	Rough Plumbing	3 wks	Tue 12/6/05	Tue 12/27/05	0%
219	Rough Electrical	3 wks	Tue 12/6/05	Tue 12/27/05	0%
220	Rough HVAC	3 wks	Tue 12/6/05	Tue 12/27/05	0%
221	Electrical Inspection	1 d	Wed 12/28/05	Wed 12/28/05	0%
222	Plumbing inspection	1 d	Wed 12/28/05	Wed 12/28/05	0%
223	Close-up inspection	1 d	Thu 12/29/05	Thu 12/29/05	0%
224	**Elevators**	**80 d**	**Fri 10/28/05**	**Thu 2/23/06**	**0%**
225	Elevator Shaft Build Out	15 d	Fri 10/28/05	Thu 11/17/05	0%
226	**Elevators**	**60 d**	**Fri 11/18/05**	**Thu 2/16/06**	**0%**
227	Rails & Doors	6 wks	Fri 11/18/05	Wed 1/4/06	0%
228	Cab	4 wks	Thu 1/5/06	Thu 2/2/06	0%
229	Adjusting & Testing	2 wks	Fri 2/3/06	Thu 2/16/06	0%
230	**Inspections for Construction Use**	**5 d**	**Fri 2/17/06**	**Thu 2/23/06**	**0%**
231	**Interiors finishes**	**121 d**	**Tue 12/6/05**	**Tue 5/30/06**	**0%**
232	Commercial Spaces - 1st Floor	6 wks	Tue 12/6/05	Wed 1/18/06	0%
233	**3rd Floor Finishes**	**72 d**	**Fri 12/16/05**	**Thu 3/30/06**	**0%**
234	Hang Drywall	10 d	Fri 12/16/05	Fri 12/30/05	0%
235	Tape & Sand	10 d	Tue 1/3/06	Mon 1/16/06	0%
236	Door Frames	5 d	Tue 1/17/06	Tue 1/24/06	0%
237	Base & Trim	5 d	Thu 1/19/06	Thu 1/26/06	0%
238	Paint (2 coats)	8 d	Fri 1/27/06	Tue 2/7/06	0%
239	Kitchen Cabinets & Millwork	7 d	Wed 2/8/06	Thu 2/16/06	0%
240	Tile & Counter tops	10 d	Mon 2/13/06	Fri 2/24/06	0%
241	Hang Doors	5 d	Wed 2/22/06	Tue 2/28/06	0%
242	MEPS Trim	10 d	Wed 2/22/06	Tue 3/7/06	0%
243	Final Paint Coat	5 d	Wed 3/8/06	Tue 3/14/06	0%
244	Final Clean-up & Contractor Punch	7 d	Wed 3/15/06	Thu 3/23/06	0%
245	Flooring (by Owner)	5 d	Fri 3/24/06	Thu 3/30/06	0%
246	**4th Floor finishes**	**72 d**	**Tue 1/3/06**	**Thu 4/13/06**	**0%**
247	Hang Drywall	2 wks	Tue 1/3/06	Mon 1/16/06	0%
248	Tape & Sand	2 wks	Tue 1/17/06	Tue 1/31/06	0%
249	Door Frames	1 wk	Wed 2/1/06	Tue 2/7/06	0%
250	Base & trim	1 wk	Fri 2/3/06	Thu 2/9/06	0%
251	Paint (2 coats)	8 d	Fri 2/10/06	Tue 2/21/06	0%
252	Kitchen Cabinets & Millwork	7 d	Wed 2/22/06	Thu 3/2/06	0%
253	Tile & Counter tops	2 wks	Mon 2/27/06	Fri 3/10/06	0%
254	Hang Doors	5 d	Wed 3/8/06	Tue 3/14/06	0%
255	MEPS Trim	2 wks	Wed 3/8/06	Tue 3/21/06	0%
256	Final Paint Coat	5 d	Wed 3/22/06	Tue 3/28/06	0%
257	Final Clean-up & Contractor Punch	7 d	Wed 3/29/06	Thu 4/6/06	0%
258	Flooring (by Owner)	1 wk	Fri 4/7/06	Thu 4/13/06	0%

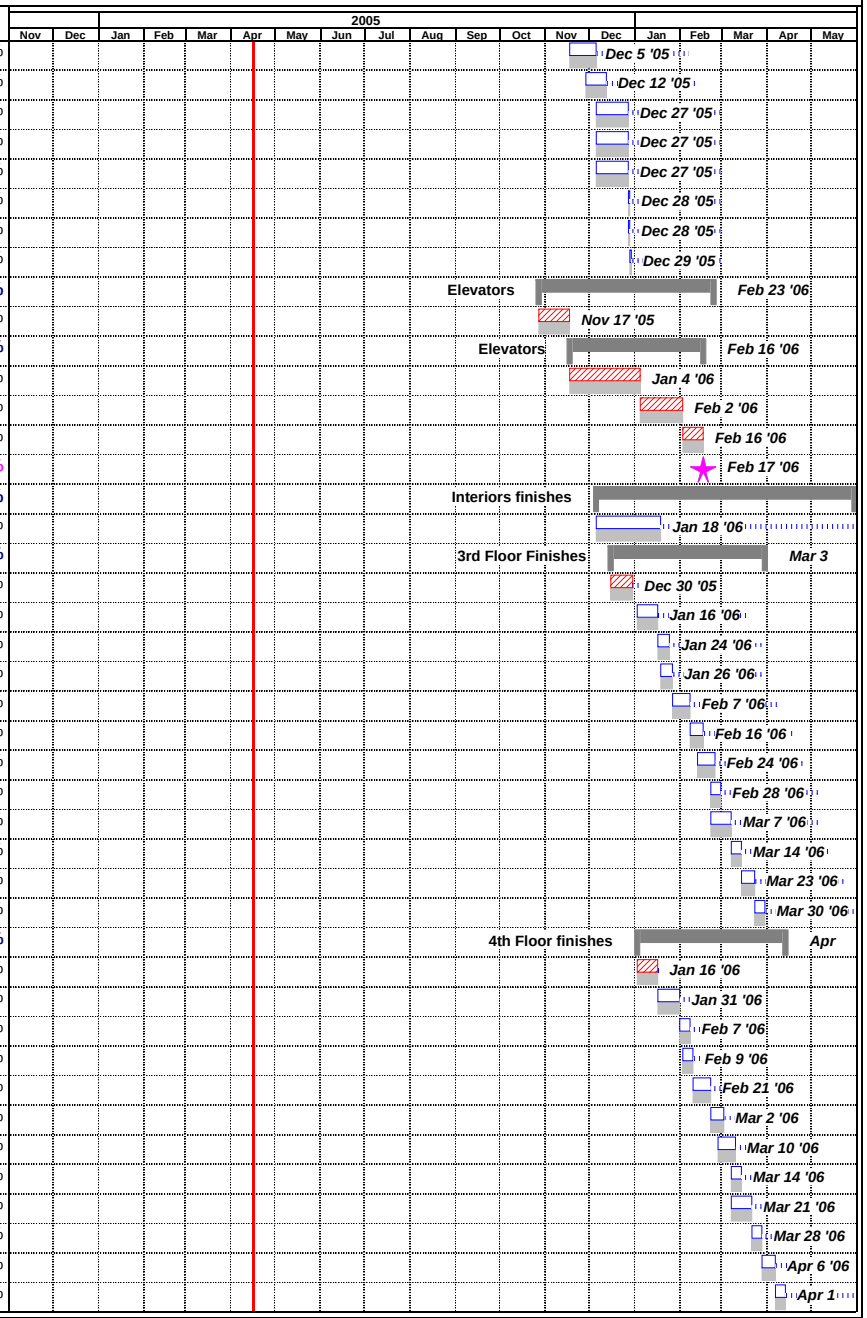

START DATE: DECEMBER 01, 2004
TCO DATE: JUNE 01, 2006
FINISH DATE: JULY 17, 2006

Actual Summary | Task | Task Progress | Actual Milestone | Deadline
Baseline | Critical Task | Baseline Milestone | Float

OWNER/DEVELOPER - THE HARBORVIEW COMPANY, LLC
CONSTRUCTION MANAGER - KSD GROUP, INC.
GENERAL CONTRACTOR - WEBCOR BUILDERS

THE HARBOR VIEW AT JACK LONDON SQUARE
121 - 129 SECOND STREET
OAKLAND, CA 94607

CONTRACT EXHIBIT "C"
STATUS DATE: April 15, 2005
Job No. 386

NO.	Name	DURATION	START	FINISH	%
259	**5th Floor finishes**	**72 d**	**Tue 1/17/06**	**Thu 4/27/06**	**0%**
260	Hang Drywall	2 wks	Tue 1/17/06	Tue 1/31/06	0%
261	Tape & Sand	2 wks	Wed 2/1/06	Tue 2/14/06	0%
262	Door Frames	1 wk	Wed 2/15/06	Tue 2/21/06	0%
263	Base & trim	1 wk	Fri 2/17/06	Thu 2/23/06	0%
264	Paint (2 coats)	8 d	Fri 2/24/06	Tue 3/7/06	0%
265	Kitchen Cabinets & Millwork	7 d	Wed 3/8/06	Thu 3/16/06	0%
266	Tile & Counter tops	2 wks	Mon 3/13/06	Fri 3/24/06	0%
267	Hang Doors	5 d	Wed 3/22/06	Tue 3/28/06	0%
268	MEPS Trim	2 wks	Wed 3/22/06	Tue 4/4/06	0%
269	Final Paint Coat	5 d	Wed 4/5/06	Tue 4/11/06	0%
270	Final Clean-up & Contractor Punch	7 d	Wed 4/12/06	Thu 4/20/06	0%
271	Flooring (by Owner)	1 wk	Fri 4/21/06	Thu 4/27/06	0%
272	**6th Floor Finishes**	**72 d**	**Wed 2/1/06**	**Thu 5/11/06**	**0%**
273	Hang Drywall	2 wks	Wed 2/1/06	Tue 2/14/06	0%
274	Tape & Sand	2 wks	Wed 2/15/06	Tue 2/28/06	0%
275	Door Frames	1 wk	Wed 3/1/06	Tue 3/7/06	0%
276	Base & trim	1 wk	Fri 3/3/06	Thu 3/9/06	0%
277	Paint (2 coats)	8 d	Fri 3/10/06	Tue 3/21/06	0%
278	Kitchen Cabinets & Millwork	7 d	Wed 3/22/06	Thu 3/30/06	0%
279	Tile & Counter tops	2 wks	Mon 3/27/06	Fri 4/7/06	0%
280	Hang Doors	5 d	Wed 4/5/06	Tue 4/11/06	0%
281	MEPS Trim	2 wks	Wed 4/5/06	Tue 4/18/06	0%
282	Final Paint Coat	5 d	Wed 4/19/06	Tue 4/25/06	0%
283	Final Clean-up & Contractor Punch	7 d	Wed 4/26/06	Thu 5/4/06	0%
284	Flooring (by Owner)	1 wk	Fri 5/5/06	Thu 5/11/06	0%
285	**7th Floor finishes**	**72 d**	**Wed 2/15/06**	**Thu 5/25/06**	**0%**
286	Hang Drywall	2 wks	Wed 2/15/06	Tue 2/28/06	0%
287	Tape & Sand	2 wks	Wed 3/1/06	Tue 3/14/06	0%
288	Door Frames	1 wk	Wed 3/15/06	Tue 3/21/06	0%
289	Base & trim	1 wk	Fri 3/17/06	Thu 3/23/06	0%
290	Paint (2 coats)	8 d	Fri 3/24/06	Tue 4/4/06	0%
291	Kitchen Cabinets & Millwork	7 d	Wed 4/5/06	Thu 4/13/06	0%
292	Tile & Counter tops	2 wks	Mon 4/10/06	Fri 4/21/06	0%
293	Hang Doors	5 d	Wed 4/19/06	Tue 4/25/06	0%
294	MEPS Trim	2 wks	Wed 4/19/06	Tue 5/2/06	0%
295	Final Paint Coat	5 d	Wed 5/3/06	Tue 5/9/06	0%
296	Final Clean-up & Contractor Punch	7 d	Wed 5/10/06	Thu 5/18/06	0%
297	Flooring (by Owner)	1 wk	Fri 5/19/06	Thu 5/25/06	0%
298	**8th Floor Finishes**	**63 d**	**Wed 3/1/06**	**Tue 5/30/06**	**0%**
299	Hang Drywall	2 wks	Wed 3/1/06	Tue 3/14/06	0%
300	Tape & Sand	2 wks	Wed 3/15/06	Tue 3/28/06	0%
301	Door Frames	1 wk	Wed 3/29/06	Tue 4/4/06	0%

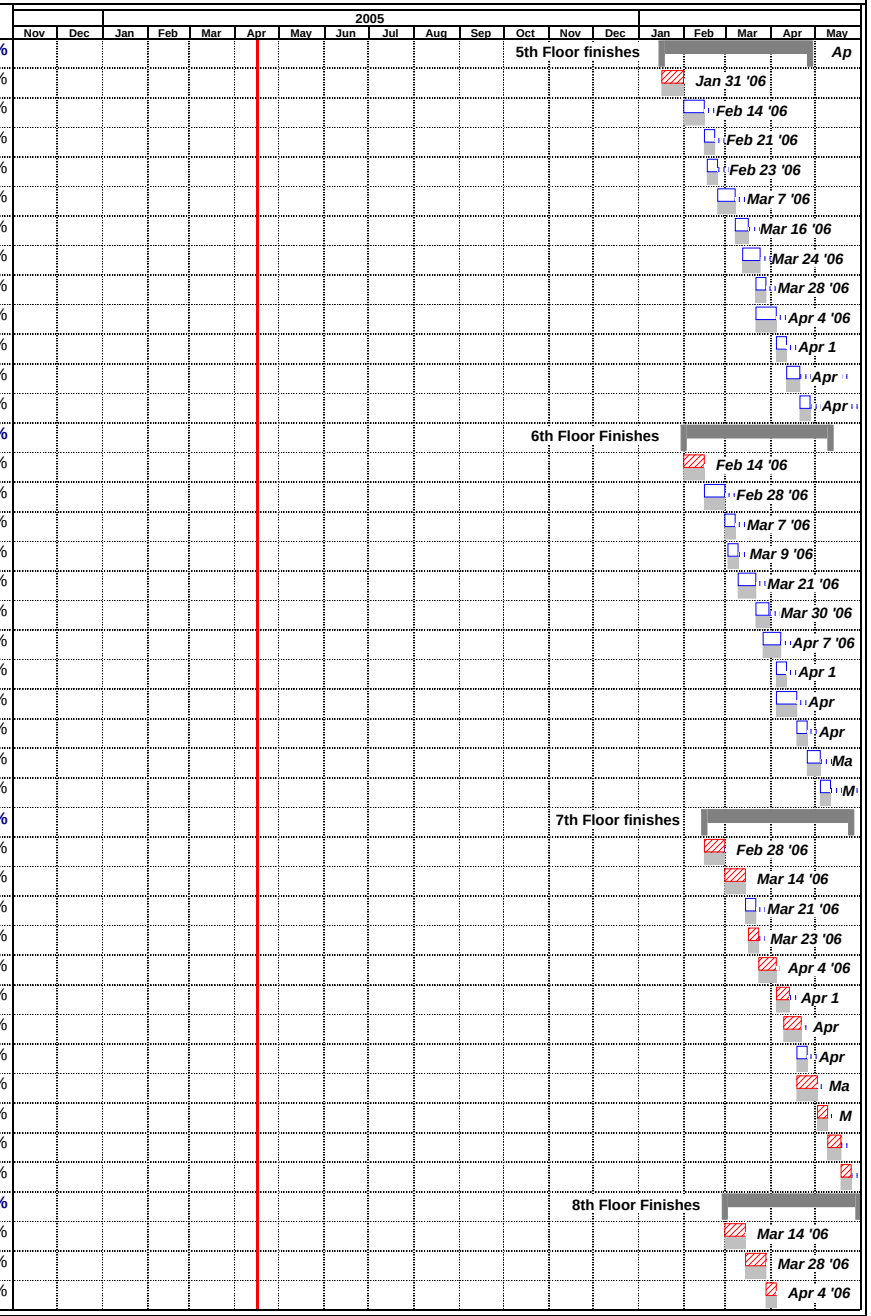

START DATE: DECEMBER 01, 2004
TCO DATE: JUNE 01, 2006
FINISH DATE: JULY 17, 2006

Actual Summary | Task | Task Progress | Actual Milestone | Deadline
Baseline | Critical Task | Baseline Milestone | Float

OWNER/DEVELOPER - THE HARBORVIEW COMPANY, LLC
CONSTRUCTION MANAGER - KSD GROUP, INC.
GENERAL CONTRACTOR - WEBCOR BUILDERS

THE HARBOR VIEW AT JACK LONDON SQUARE

121 - 129 SECOND STREET
OAKLAND, CA 94607

CONTRACT EXHIBIT "C"
STATUS DATE: April 15, 2005
Job No. 386

NO.	Name	DURATION	START	FINISH	%
302	Base & trim	1 wk	Fri 3/31/06	Thu 4/6/06	0%
303	Paint (2 coats)	8 d	Wed 4/5/06	Fri 4/14/06	0%
304	Kitchen Cabinets & Millwork	7 d	Thu 4/13/06	Fri 4/21/06	0%
305	Tile & Counter tops	1 wk	Tue 4/18/06	Mon 4/24/06	0%
306	Hang Doors	5 d	Thu 4/20/06	Wed 4/26/06	0%
307	MEPS Trim	2 wks	Thu 4/20/06	Wed 5/3/06	0%
308	Final Paint Coat	5 d	Thu 5/4/06	Wed 5/10/06	0%
309	Final Clean-up & Contractor Punch	7 d	Thu 5/11/06	Fri 5/19/06	0%
310	Flooring (by Owner)	1 wk	Mon 5/22/06	Tue 5/30/06	0%
311	Lobby & Corridor Build-Out & Finishes	8 wks	Wed 3/15/06	Tue 5/9/06	0%
312	**Commissioning & Inspections**	**15 d**	**Thu 4/20/06**	**Wed 5/10/06**	**0%**
313	Equipment startup & inspection	3 wks	Thu 4/20/06	Wed 5/10/06	0%
314	Preliminary Fire life safety inspections	1 wk	Thu 5/4/06	Wed 5/10/06	0%
315	**Final Inspection**	**14 d**	**Thu 5/11/06**	**Thu 6/1/06**	**0%**
316	Elevator Finals	1 wk	Fri 5/12/06	Thu 5/18/06	0%
317	Plumbing	2 wks	Thu 5/11/06	Wed 5/24/06	0%
318	Electrical	2 wks	Thu 5/11/06	Wed 5/24/06	0%
319	Fire	2 wks	Thu 5/11/06	Wed 5/24/06	0%
320	Building	2 wks	Wed 5/17/06	Thu 6/1/06	0%
321	**Building TCO (Substantial Completion)**	**0 wks**	**Thu 6/1/06**	**Thu 6/1/06**	**0%**
322	Clean-up & Final Punchlist	6 wks	Fri 6/2/06	Mon 7/17/06	0%
323	**Final Completion**	**0 wks**	**Mon 7/17/06**	**Mon 7/17/06**	**0%**

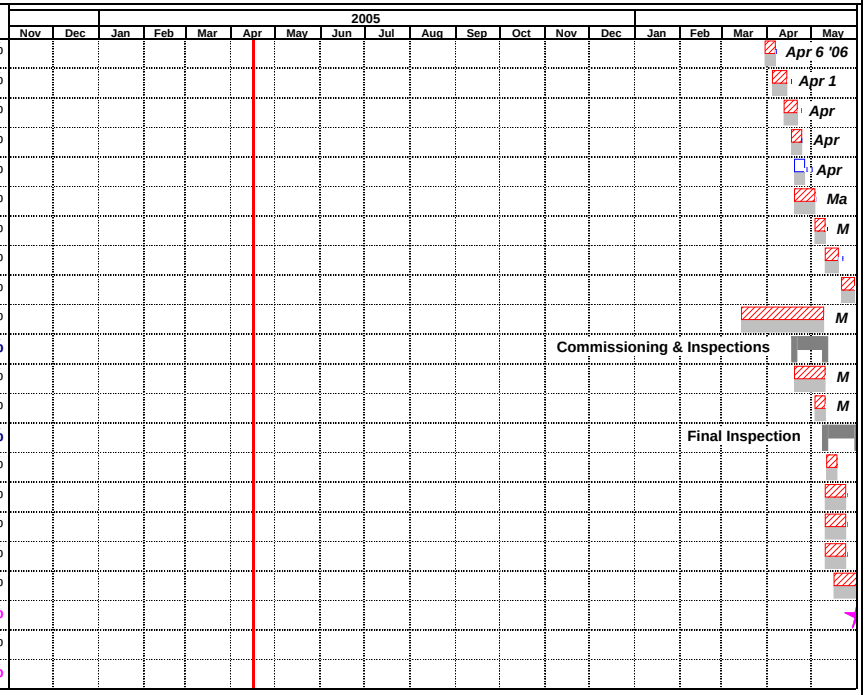

START DATE: DECEMBER 01, 2004
TCO DATE: JUNE 01, 2006
FINISH DATE: JULY 17, 2006

Actual Summary | Task | Task Progress | Actual Milestone | Deadline
Baseline | Critical Task | Baseline Milestone | Float
